

Smart Grid Investment Grant Project Update

Jim McNierney

Enterprise Architect
New York Independent System Operator
jmcnierney@nyiso.com

NASPI Work Group Meeting

October 12-13, 2011 San Francisco, CA





Acknowledgment & Disclaimer

- **Acknowledgment:** This material is based upon work supported by the Department of Energy under Award Number(s) DE-OE0000368
- **Disclaimer:** This report was prepared as an account of work sponsored by an agency of the United States Government. Neither the United States Government nor any agency thereof, nor any of their employees, makes any warranty, express or implied, or assumes any legal liability or responsibility for the accuracy, completeness, usefulness of any information, apparatus, product, or process disclosed, or represents that its use would not infringe privately owned rights. Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof. The views and opinions of authors expressed herein do not necessarily state or reflect those of the United States Government or any agency thereof.



Project Participants

- New York ISO
 - Project Manager Kathleen Dalpe
 - kdalpe@nyiso.com
 - (518) 356-7657
 - Business Owner Rich Dewey, Senior Vice President & Chief Information Officer





Project Participants

New York Transmission Owners (TOs)

- Central Hudson Electric & Gas
 - 1 PMU, 1 PDC
- Consolidated Edison
 - 14 PMUs, 2 PDCs
- Long Island Power Authority
 - 2 PMUs, 1 PDC
- National Grid
 - 12 PMUs, 1 PDC
- New York Power Authority
 - 4 PMUs, 2 PDCs
- New York State Electric & Gas
 - 5 PMUs, 1 PDC
- Rochester Gas & Electric
 - 1 PMU, 1 PDC





Project Participants

- Quanta Technologies, Inc.
 - Crowe Horwath LLP
 - PMOLink LLC
- EPRI
- EnerNex
- ABB





Project Timeline

Location	Activity Name	KV Level	Units	Inits Start	Finish	Remaining Units		2012				
							Q4	Q1	Q2	Q3	Q4	Q1
■ Capacitors			804	11-Sep-11	15-Feb-13		22	94	88	89	495	16
⊞ ■ Central Hudsor	1		35	11-Sep-11	30-Jun-12		22		13			
🗷 🔜 National Grid			286	11-Sep-11	31-Dec-12			70	61	55	100	0
⊞ ■ NYSEG			320	04-Jun-12	31-Dec-12						320	
= ₹ 0&R				11-Jun-12	15-Feb-13				14	34		16
[⊞] ♥ RGE			99	15-Sep-11	31-Dec-12			24			75	
■ PDC			9	11-Sep-11	09-Aug-12		2	3	2	2		
🗷 🔜 Central Hudsor	1		1	01-Nov-11	30-Jun-12				1	0		
≖ 尽 ConEd			2	11-Sep-11	30-Mar-12		1	1				
≖ 尽 LIPA			1	01-0 ct-11	31-Dec-11		1					
🗷 🔜 National Grid			1	11-Sep-11	31-Jul-12					1		
⊞ ♥ NYPA			2	02-Jan-12	15-Jan-12			2				
■ ■ NYSEG			1	28-Jun-12	09-Aug-12					1		
≖ ■ RGE			1	19-Apr-12	31-May-12				1			
■ PMU			39	24-May-11 A	v 07-Jan-13		5	6	10	15	1	2
🗷 🔜 Central Hudsor	1			01-Nov-11	30-Jun-12				1	0		
≖ ▼ ConEd			14	24-May-11 A	30-Sep-12		3	4	6	1		
≖ ♥ LIPA			2	01-0 ct-11	31-Dec-11		2					
🗷 🔜 National Grid				01-Apr-12	31-Jul-12					12		
≖ 尽 NYPA				01-Feb-12	18-May-12			2	2			
■ ■ NYSEG			5	17-May-12	07-Jan-13					2	1	2
[⊕] ♥ RGE			1	08-Mar-12	31-May-12				1			





Project Timeline

Activity ID Activity Name	Current Start	Current Finish			2012				2013		
Y .			Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
■	02-Aug-10 A	11-Jan-13							11-Jan-13		
🛚 🛂 Situational Awareness (Visualization) Applications	09-Aug-10 A	16-Nov-12						16-N	lov-12		
🛮 🛂 System Studies - Calibration and Validation of Dynamic Models	24-Sep-10 A	31-0ct-12						31-Oct	-12		
🛨 🛂 System Studies - Controlled System Separation	02-Aug-10 A	11-Jan-13							11 Jan-13		
■	20-Sep-10 A	16-0ct-12						16-Oct-1	2		
📲 🛂 PMU Enhanced State Estimator Applications	20-Sep-10 A	23-Oct-12				1		23-Oct-	12		





Phasor Measurement Units

- Seven TO organizations in project
 - Total of 50 PMUs (39 new + 11 existing)
 - Each TO is selecting its own PMU equipment from common minimum requirements set by the project
- PMU placement study dictated what signals were to be monitored at each location
- Number of substations with PMUs -- 50
- Sample rate -- 60 samples per second
- Range of PMUs being installed
 - Disturbance Fault Recorders (DFRs)
 - Dynamic Disturbance Recorders (DDRs)
 - Stand-alone





Phasor Measurement Units

- Installation rate
 - Installing 39 new PMUs by EOY 2012 and folding in 11 existing PMUs





PDCs and Communications

- Phasor Data Concentrators (PDCs)
 - ISO control centers
 - TO primary control centers
 - Some TO secondary control centers
 - One field PDC
- Archive
 - Envisioned to hold Real-Time, one year of full resolution data, seven years of event specific data





PDCs and Communications

- Communications System
 - Communication links to TOs will be fiber based from two separate Telecomm vendors
 - Virtual Private LAN Service (VPLS) cloud-based architecture
 - Managed by NYISO





Major Project Goals

- Low Frequency Oscillation Monitor
- Voltage Stability Monitor
- Offline Study for model calibration
- Offline Study of viability of Controlled System Separation





Major Application Goals

- All TOs will have access to visualization apps through TO portal
- Wide Area Situational Awareness (WASA) will be provided through third-party vendor - TBD
- Phasor enhanced State Estimation function planned to begin validation in 2012
- Hardware and software installations scheduled to be complete by 4th quarter 2012






Challenges & Lessons Learned

- Biggest technical challenges to date?
 - Changing Standards / Future Proofing
 - Calibration of Signals / Testing





The New York Independent System Operator (NYISO) is a not-for-profit corporation responsible for operating the state's bulk electricity grid, administering New York's competitive wholesale electricity markets, conducting comprehensive long-term planning for the state's electric power system, and advancing the technological infrastructure of the electric system serving the Empire State.

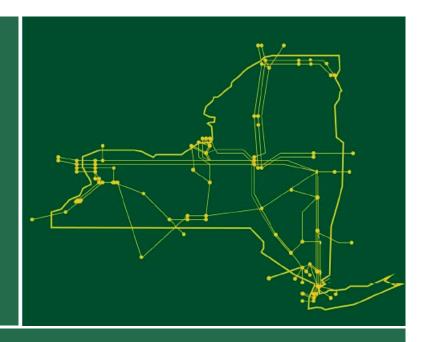

www.nyiso.com
